

Weekly Status Report

Week of May 27, 2024

Completed Activities

Week of May 20 2024:

Cable Route

Long Island Expressway(495) South Service Road (NYSDOT Working hours 10AM – 3PM , 10PM – 6AM)

The contractor activities include:

- Continuing trenching and conduit installation activities
- Continuing temporary road restoration
- Continuing vault installation (Potential 8PM start)

AC Route within PSEG-LI right of way

The contractor activities include:

- Continuing trenching and conduit installation activities
- Beginning mobilization for trenchless crossing

Union Avenue Onshore Converter Station

The contractor's activities include:

- Continuing build out interior of buildings
- Installation of below grade facilities
- Continuing erecting building structures
- Continuing installation of retaining wall
- Continuing backfilling and grading

Holbrook Substation Expansion

The contractor's activities include:

- Continuing pouring foundations
- Continuing site grading
- Continuing substation civil works
- Continuing installation of retaining wall
- Continuing build out interior of buildings

Weekly Status Report

Week of May 27, 2024

Upcoming Activities

Week of May 27, 2024:

Cable Route

Long Island Expressway(495) South Service Road (NYSDOT Working hours 10AM – 3PM , 10PM – 6AM)

The contractor intends to:

- Continue trenching and conduit installation activities
- Continue temporary road restoration
- Continue vault installation (Potential 8PM start)

AC Route within PSEG-LI right of way

The contractor activities include:

- Continue trenching and conduit installation activities
- Continue mobilization for trenchless crossing

Union Avenue Onshore Converter Station

The contractor intends to:

- Continue build out interior of buildings
- Continue installation of below grade facilities
- Continue erecting building structures
- Continue installation of retaining wall
- Continue backfilling and grading

Holbrook Substation Expansion

The contractor intends to:

- Continue pouring foundations
- Continue site grading
- Continue substation civil works
- Continue installation of retaining wall
- Continue build out interior of buildings

Weekly Status Report

Week of May 27, 2024

Week of June 3, 2024:

Cable Route

Long Island Expressway(495) South Service Road (NYS DOT Working hours 10AM – 3PM , 10PM – 6AM)

The contractor intends to:

- Continue trenching and conduit installation activities
- Continue temporary road restoration
- Continue vault installation (Potential 8PM start)

AC Route within PSEG-LI right of way

The contractor intends to:

- Continue trenching and conduit installation activities
- Begin excavation and prep for trenchless crossing

Union Avenue Onshore Converter Station

The contractor intends to:

- Continue build out interior of buildings
- Continue installation of below grade facilities
- Continue erecting building structures
- Continue installation of retaining wall
- Continue backfilling and grading

Holbrook Substation Expansion


The contractor intends to:

- Continue pouring foundations
- Continue site grading
- Continue substation civil works
- Continue installation of retaining wall
- Continue build out interior of buildings

Weekly Status Report

Week of May 27, 2024

Laydown yards will continue to be used for utility, storage, and parking.

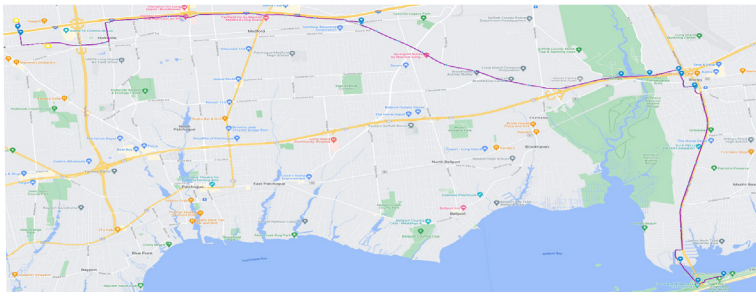

[Click here to view the construction progress map.](#)

-  Active construction
-  Temporary restoration
-  Completed restoration

If you have any questions about any information contained in this notice or any other Project-related matter, please call our hotline at 631-629-8410 or email us at info@sunrisewindny.com.

**Best Regards,
The Sunrise Wind Team**

Website: www.Sunrisewindny.com

Follow us on Twitter: @Sunrisewindny

Hotline: 631-629-8410

Email: info@sunrisewindny.com
