

# Weekly Status Report

## Week of June 17, 2024

### Completed Activities

#### Week of June 10, 2024:

##### Cable Route

**Long Island Expressway(495) South Service Road (NYSDOT Working hours 10AM – 3PM , 10PM – 6AM)**

The contractor activities include:

- Continuing trenching and conduit installation activities
- Continuing temporary road restoration

##### AC Route within PSEG-LI right of way

The contractor activities include:

- Continuing trenching and conduit installation activities
- Continuing excavation and prep for trenchless crossing
- Continuing installing a temporary access road on north side of PSEG-LI ROW

##### Union Avenue Onshore Converter Station

The contractor's activities include:

- Continuing build out interior of buildings
- Installation of below grade facilities
- Continuing installation of retaining wall
- Continuing backfilling and grading

##### Holbrook Substation Expansion

The contractor's activities include:

- Continuing pouring foundations
- Continuing site grading
- Continuing substation civil works
- Continuing installation of retaining wall
- Continuing build out interior of buildings

# Weekly Status Report

## Week of June 17, 2024

### Upcoming Activities

#### Week of June 17, 2024:

##### Cable Route

**Long Island Expressway(495) South Service Road (NYSDOT Working hours 10AM – 3PM , 10PM – 6AM)**

The contractor intends to:

- Continue trenching and conduit installation activities
- Continue temporary road restoration

##### AC Route within PSEG-LI right of way

The contractor activities include:

- Continue trenching and conduit installation activities
- Begin trenchless crossing activities

##### Union Avenue Onshore Converter Station

The contractor intends to:

- Continue build out interior of buildings
- Continue installation of below grade facilities
- Continue installation of retaining wall
- Continue backfilling and grading

##### Holbrook Substation Expansion

The contractor intends to:

- Continue pouring foundations
- Continue site grading
- Continue substation civil works
- Continue installation of retaining wall
- Continue build out interior of buildings

# Weekly Status Report

## Week of June 17, 2024

### **Week of June 24, 2024:**

#### **Cable Route**

**Long Island Expressway(495) South Service Road (NYSDOT Working hours 10AM – 3PM , 10PM – 6AM)**

The contractor intends to:

- Continue trenching and conduit installation activities
- Continue temporary road restoration

#### **AC Route within PSEG-LI right of way**

The contractor intends to:

- Continue trenching and conduit installation activities
- Continue trenchless crossing activities

#### **DC Route (Anticipated start on or after June 24th)**

The contractor intends to:

- Begin sawcutting

#### **Union Avenue Onshore Converter Station**

The contractor intends to:

- Continue build out interior of buildings
- Continue installation of below grade facilities
- Continue backfilling and grading

#### **Holbrook Substation Expansion**

The contractor intends to:

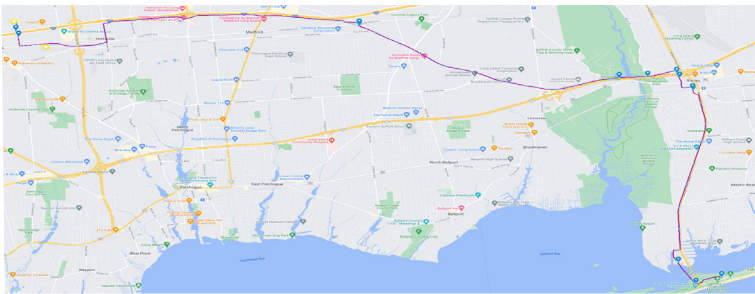
- Continue pouring foundations

# Weekly Status Report




## Week of June 17, 2024

- Continue site grading
- Continue substation civil works
- Continue installation of retaining wall
- Continue build out interior of building

*Laydown yards will continue to be used for utility, storage, and parking.*



[Click here to view the construction progress map.](#)

-  Active construction
-  Temporary restoration
-  Completed restoration

If you have any questions about any information contained in this notice or any other Project-related matter, please call our hotline at 631-629-8410 or email us at [info@sunrisewindny.com](mailto:info@sunrisewindny.com).

**Best Regards,  
The Sunrise Wind Team**

**Website:** [www.Sunrisewindny.com](http://www.Sunrisewindny.com)

**Follow us on Twitter:** @Sunrisewindny

**Hotline:** 631-629-8410

**Email:** [info@sunrisewindny.com](mailto:info@sunrisewindny.com)
