

Weekly Status Report

Week of March 25, 2024

Completed Activities

Week of March 18 2024:

Union Avenue Onshore Converter Station

The contractor's activities include:

- Continuing excavation for foundations
- Continuing pouring foundations
- Continuing build out interior of buildings
- Installation of below grade facilities
- Continuing erecting building structures

Holbrook Substation Expansion

The contractor's activities include:

- Continuing pouring foundations within substation
- Continuing site grading

Upcoming Activities

Week of March 25, 2024:

Cable Route

Long Island Expressway(495) South Service Road (NYSDOT Working hours 10AM – 3PM , 10PM – 6AM)

The contractor intends to:

- Begin sawcutting
- Begin trenching and conduit installation activities
- Begin temporary road restoration

Weekly Status Report

Week of March 25, 2024

Union Avenue Onshore Converter Station

The contractor intends to:

- Continue excavation for foundations
- Continue pouring foundations
- Continue build out interior of buildings
- Continue installation of below grade facilities
- Continue erecting building structures
- Accepting oversized deliveries

Holbrook Substation Expansion

The contractor intends to:

- Continue pouring foundations
- Continue site grading
- Begin substation civil works

Week of April 1, 2024:

Cable Route

Long Island Expressway(495) South Service Road (NYS DOT Working hours 10AM – 3PM , 10PM – 6AM)

The contractor intends to:

- Continue sawcutting
- Continue trenching and conduit installation activities
- Begin vault installation
- Continue temporary road restoration

Union Avenue Onshore Converter Station

The contractor intends to:

- Continue excavation for foundations
- Continue pouring foundations
- Continue build out interior of buildings

Weekly Status Report

Week of March 25, 2024

- Continue installation of below grade facilities
- Continue erecting building structures
- Accepting oversized deliveries


Holbrook Substation Expansion

The contractor intends to:


- Continue pouring foundations
- Continue site grading
- Continue substation civil works
- Begin installation of retaining wall

Laydown yards will continue to be used for utility, storage, and parking.

If you have any questions about any information contained in this notice or any other Project-related matter, please call our hotline at 631-629-8410 or email us at info@sunrisewindny.com.

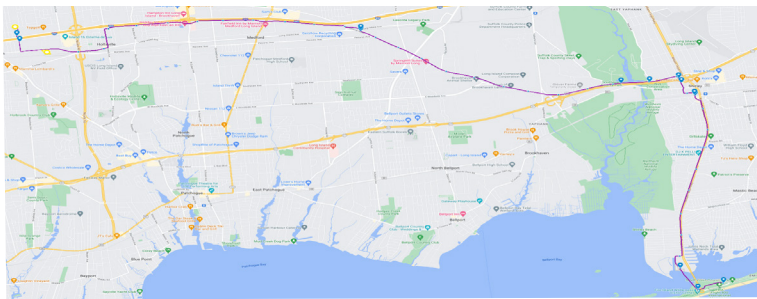

[Click here to view the construction progress map.](#)

-  Active construction
-  Temporary restoration
-  Completed restoration

**Best Regards,
The Sunrise Wind Team**

Website: www.Sunrisewindny.com

Follow us on Twitter: @Sunrisewindny

Hotline: 631-629-8410

Email: info@sunrisewindny.com
